

S James Street & SE 37th Street Improvements

Weekly Construction Update – Grimes, IA



The intent of this weekly update is to give an overview of work completed and a projection of work in the following week. It is intended to be a general overview and be tentative in nature. Things may differ from the listed schedule if weather or other unknown factors come into play.

Weekly Overview: October 1 Monday – October 6 Saturday

- Paving of the median caps has been completed.
- The contractor paved the mainline of S James Street north of SE 37th Street.
- Conduit and signal pole bases for the traffic signals were installed.
- Grading was completed for the recreational trail, and paving has been started.

What to expect next week: October 8 Monday – October 13 Saturday


- Phase 4 traffic control will continue to be in place.
- Weather pending, traffic is planned to shift Friday, October 12, in order to complete paving work on existing southbound pavement. See the attached figure for the proposed traffic control plan.
- Trail work will continue adjacent to S James Street.
- Striping will be completed on S James Street and SE 37th Street.
- Traffic signal poles will be installed.
- Traffic loops will be installed.

What you need to know:


- Working hours are Monday-Friday (7:00 am to 9:00 pm). Work on the weekends and at night will require City approval.
- The contractor will notify property owners if work will impact access to property.
- Please do not remove any construction stakes located within the limits of work.
- During construction if property owners lose utility service, please contact your local service provider as follows:
 - Electric - MidAmerican Energy 1-888-427-5632
 - Gas - Black Hills Energy 1-888-890-5554
 - Cable, Internet, Telephone
 - CenturyLink 1-866-642-0444
 - Mediacom 1-800-332-0245
 - Sewer / Water – US Water
1-515-968-3176 (regular business hours)
1-515-822-4671 (emergency after hours)
- Construction projects are fluid in nature, and depend on many variables. Examples are poor weather, utility conflicts, unknown underground items, and fabrication schedules. While we will do our best to meet planned schedules, we appreciate your patience with unforeseen circumstances and understanding the possibility of changes to the schedule.

If you have any questions, please contact John Gade with FOX Engineering at 515-233-0000 or by email at jmg@foxeng.com.



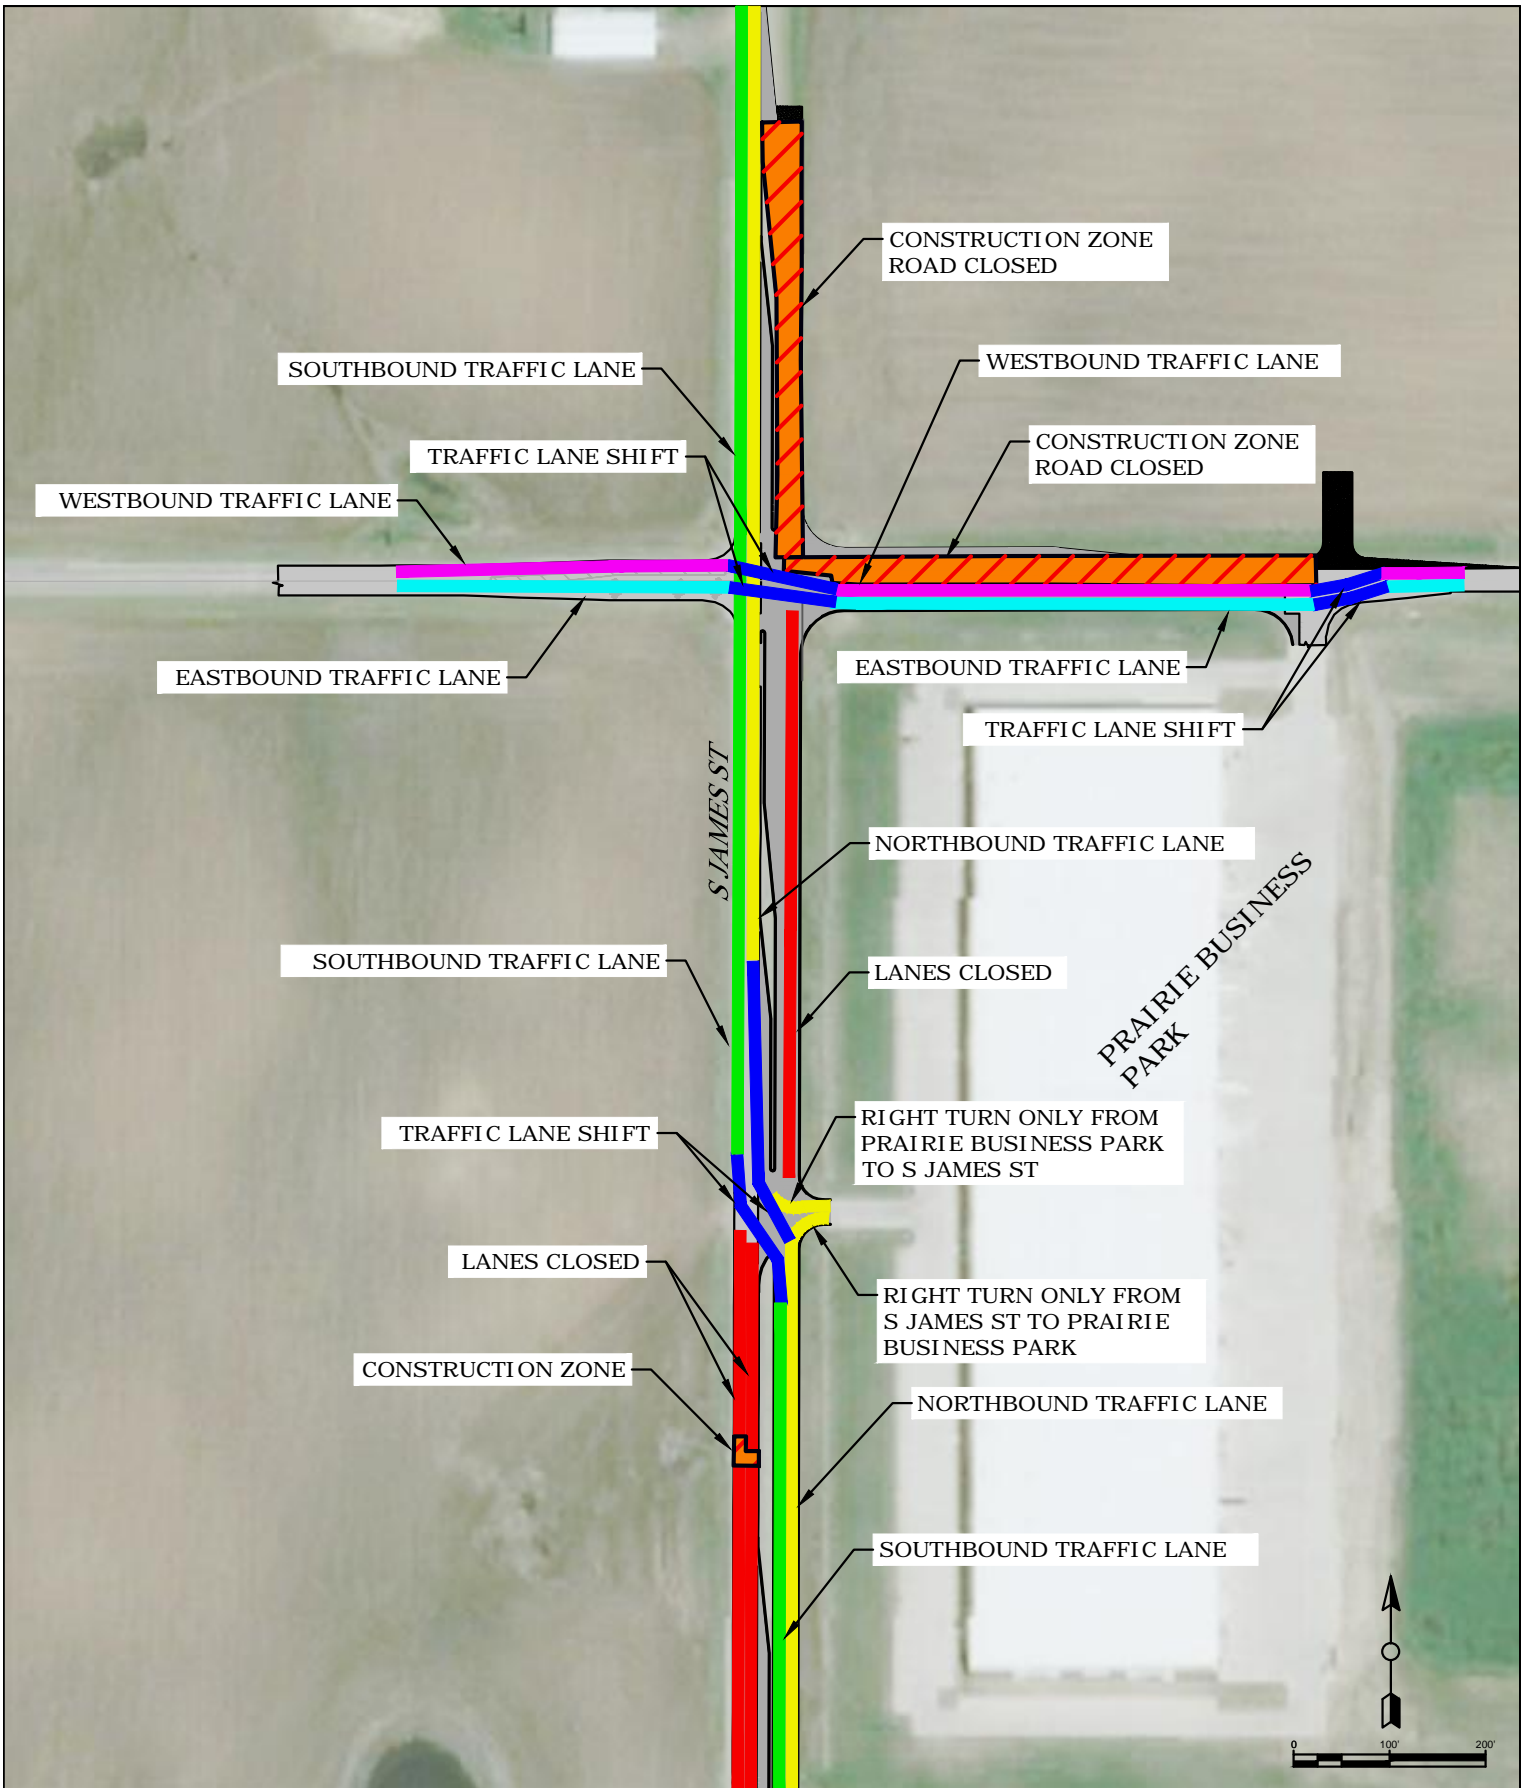

S JAMES & SE 37TH ST IMPROVEMENTS PROJECT
 PHASE 5A TRAFFIC CONTROL

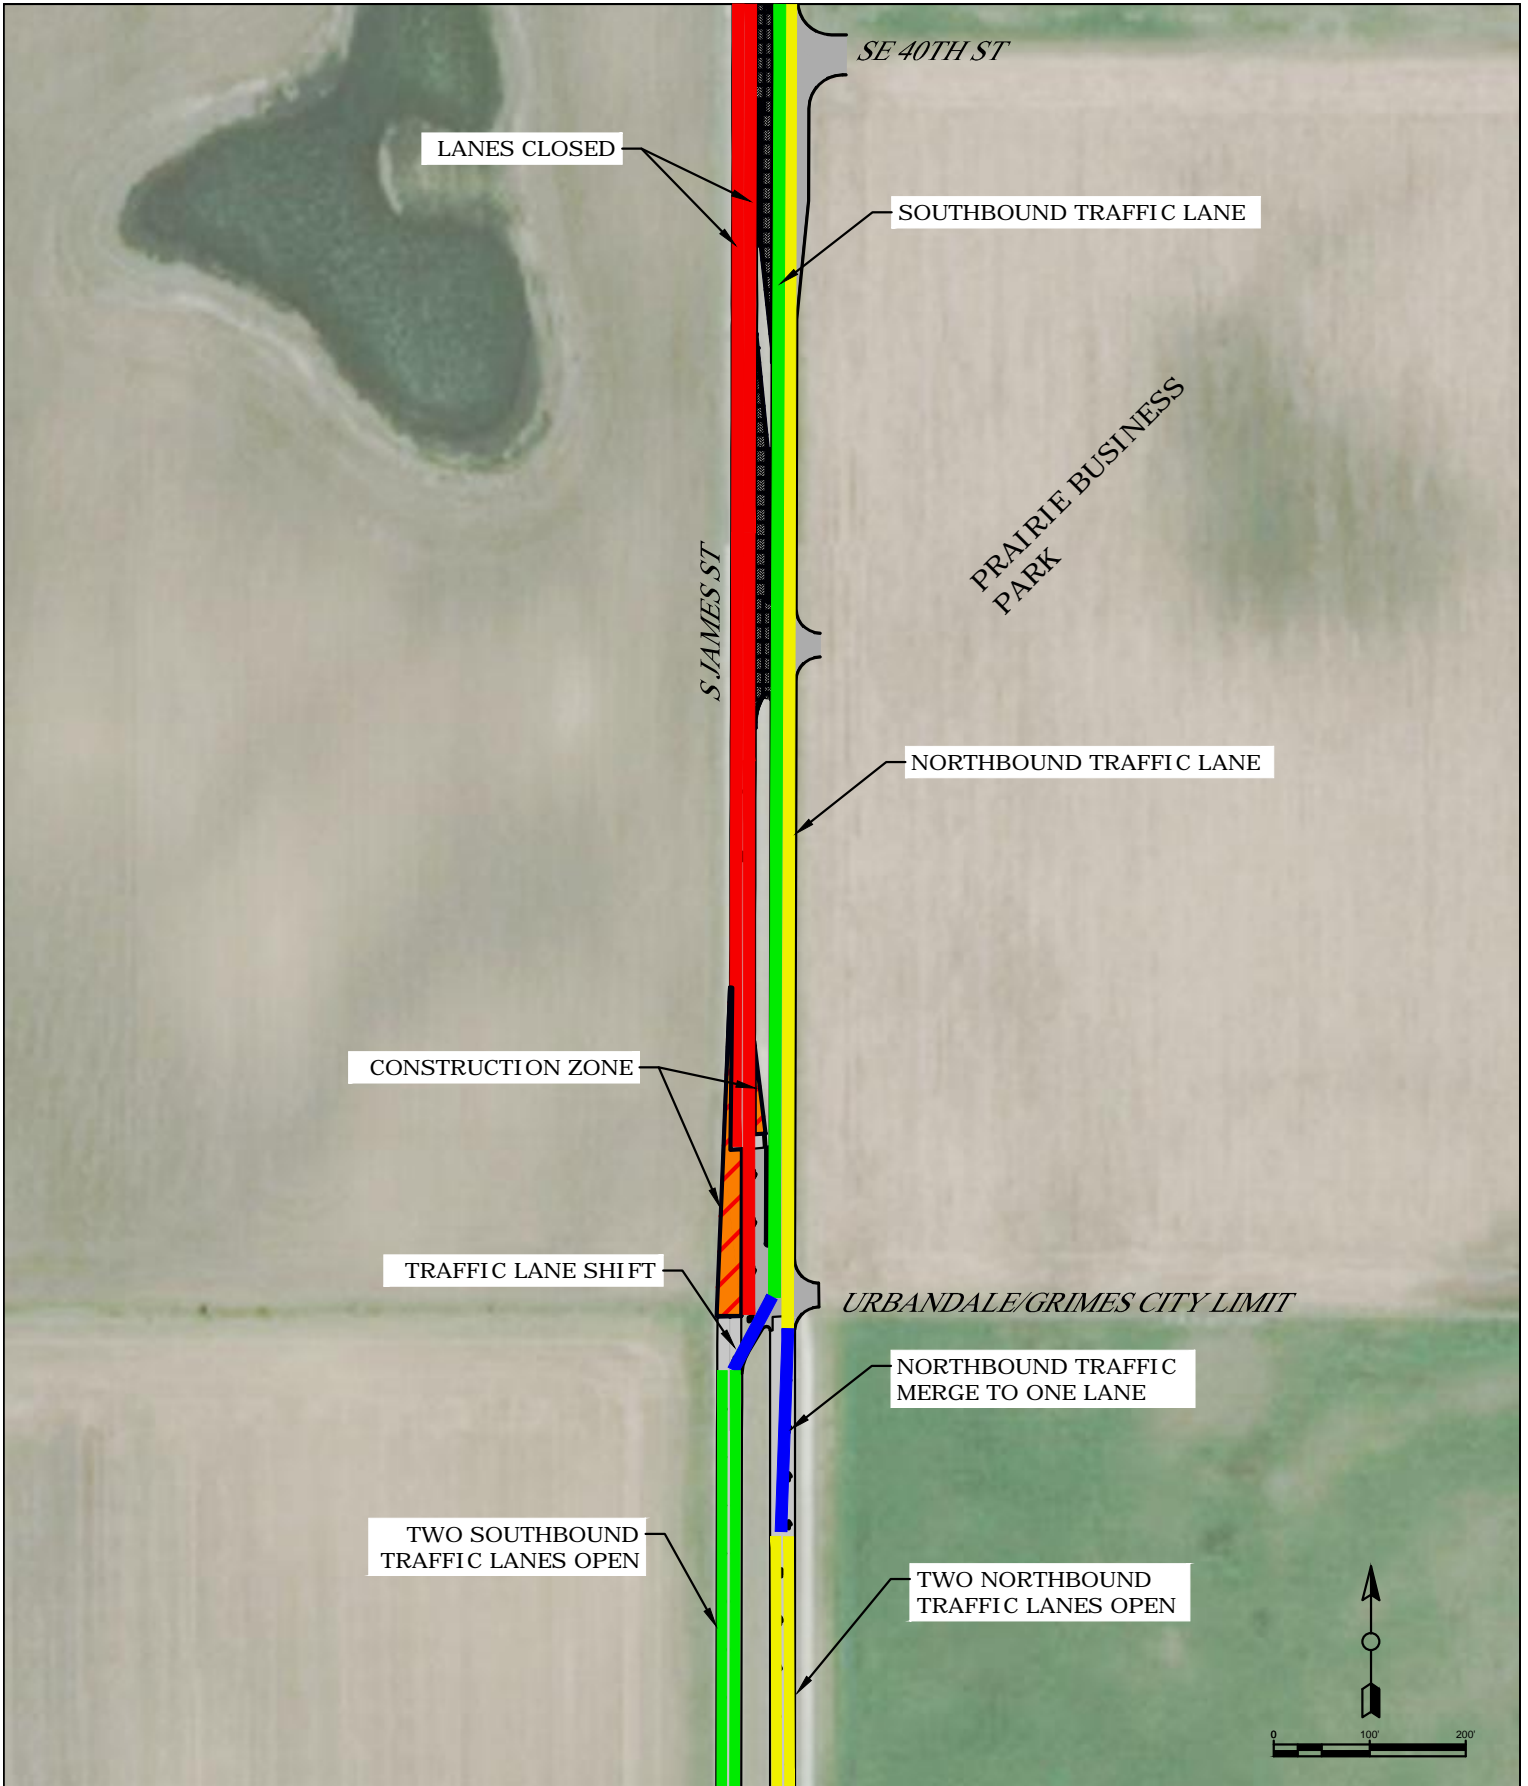

S JAMES & SE 37TH ST IMPROVEMENTS PROJECT
 PHASE 5A TRAFFIC CONTROL
